

City Side Development Project at **Chaudhary Charan Singh International Airport, Lucknow** – Design and Build



Monthly Review Meeting 06 ~ Sep'26



Dated : 03-Sep-26



**SAFETY
FIRST**



**QUALITY
ALWAYS**



**COLLABORATE
TO WIN**



**DELIVER
EXCELLENCE**





Attention everyone: We are currently in the conference hall of the Terminal-2 building.



In case of any emergency,

- Please remain calm and do not panic.



- Evacuate the area immediately by following the marked emergency exit routes.



Proceed calmly to the nearest **assembly point** located outside the building, behind the Chaudhary Charan Singh statue.



STAY CALM
Do not panic



FOLLOW EXIT ROUTES
Use the marked emergency exits



ASSEMBLE SAFELY
Reach the assembly point



WAIT FOR INSTRUCTIONS
Follow instructions from the authorities

Safety Pledge

“On this Day, I solemnly affirm that I will rededicate myself to the cause of the safety, health and protection of environment, will do my best to observe rules, regulations and procedures and develop attitudes and habits conducive for achieving these objectives.

I fully realize that accidents and occupational diseases are a drain on the national economy and may lead to disablement, death, harm to health, damage to property, social suffering and general degradation of environment.

I will do everything possible for the prevention of accidents, occupational diseases and protection of environment in the interest of self, family, organization, community and the nation at large”.



Quality Pledge



I take a pledge to assure that I shall remain
Quality conscious and diligent in executing my
duties to achieve Quality in Process, Product &
Services at every stage of my work, promoting a
“First Time Right, Every Time” culture.

Together, we will strive to achieve excellence in
every aspect of our work, ensuring the highest
standards of quality for our customers,
stakeholders and Organization as a Whole.



Executive Dashboard

ADANI LUCKNOW AIRPORT CITY · MONTHLY REVIEW · AUGUST 2026

CONTRACT VALUE

₹1,725 Cr

39-MONTH CONTRACT

DURATION

39 Months

COMMENCED FEB 2026

COMPLETION

15 May 2029

CONTRACTUAL TARGET

PROJECT HEALTH

WATCHLIST

COMMERCIAL SLIPPAGE

■ COMMERCIAL PROGRESS ₹ Cr

FTM

15.5

CUM

37.8

■ ACTUAL

■ REVAMP PLAN

■ BASELINE

FTM VS BASELINE

-61%

₹24.50 Cr short

CUM VS BASELINE

-67%


₹76.20 Cr short

GAP TO CLOSE

₹76.2 Cr

33 months remaining

■ SAFETY & QUALITY

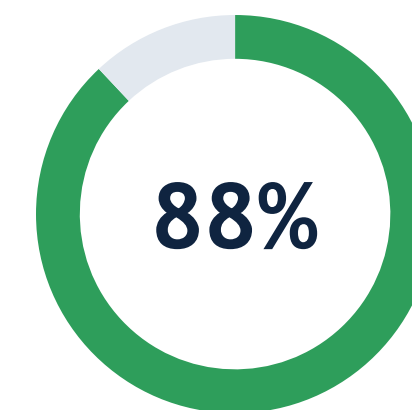

FTRI SCORE

3,44,498

SAFE MANHOURS · ITD

0

LOST TIME INJURIES

WIR 118 / 26

MIR 63 / 1

NEAR MISSES



INDUCTIONS



OPEN NCR



CRITICAL ISSUES

Alternate batching-plant operation delay

Work-front handover incomplete

RT-1 handover 24 Aug vs BL 16 Jun 26

KEY DECISION

Alternate concrete supplier approved

for 5,000 m³ on 31 August 2026.

SUPPORT REQUESTED

Adhoc payment vs RA bills within 15 days

100% payment for concrete supply

Supply RA bills within 21 days

Internal

TATA

TATA PROJECTS

GFC Drawings Status

RELEASE PROGRAMME BY DISCIPLINE · AUGUST 2026

Turner & Townsend

adani

FOUNDATION

R0 ISSUED

OPTIMISED REVISION 20 AUG

STRUCTURAL GFC

3 OF 5

RELEASED TO DATE

ARCHITECTURAL GFC

22-29 SEP

B3 / B2 / B1 WINDOW

MEPF GFC

22 SEP-14 OCT

B3 THROUGH GF

STRUCTURAL GFC RELEASE

Foundation	20 Aug	ISSUED
Basement 03	20 Aug	EARLY
Basement 02	31 Aug	ON PLAN
Basement 01	18 Sep	SCHEDULED
Ground Floor	14 Oct	ON PLAN

ARCHITECTURAL GFC RELEASE

Basement 03	22 Sep	SCHEDULED
Basement 02	22 Sep	SCHEDULED
Basement 01	29 Sep	SCHEDULED
B3 centre line issued 01 Jun		
B2 centre line issued 20 Jul		

MEPF GFC RELEASE


Basement 03	22 Sep	SCHEDULED
Basement 02	22 Sep	SCHEDULED
Basement 01	29 Sep	SCHEDULED
Ground Floor	14 Oct	ON PLAN

FOUNDATION GFC RELEASE NOTE

R0 issued 27 May 2026; optimised revision issued 20 August 2026.

Structural GFC for Basement 03 released early against plan; Basement 02 tracking on plan for 31 August.

Peer review approval is the gate for the remaining structural releases.

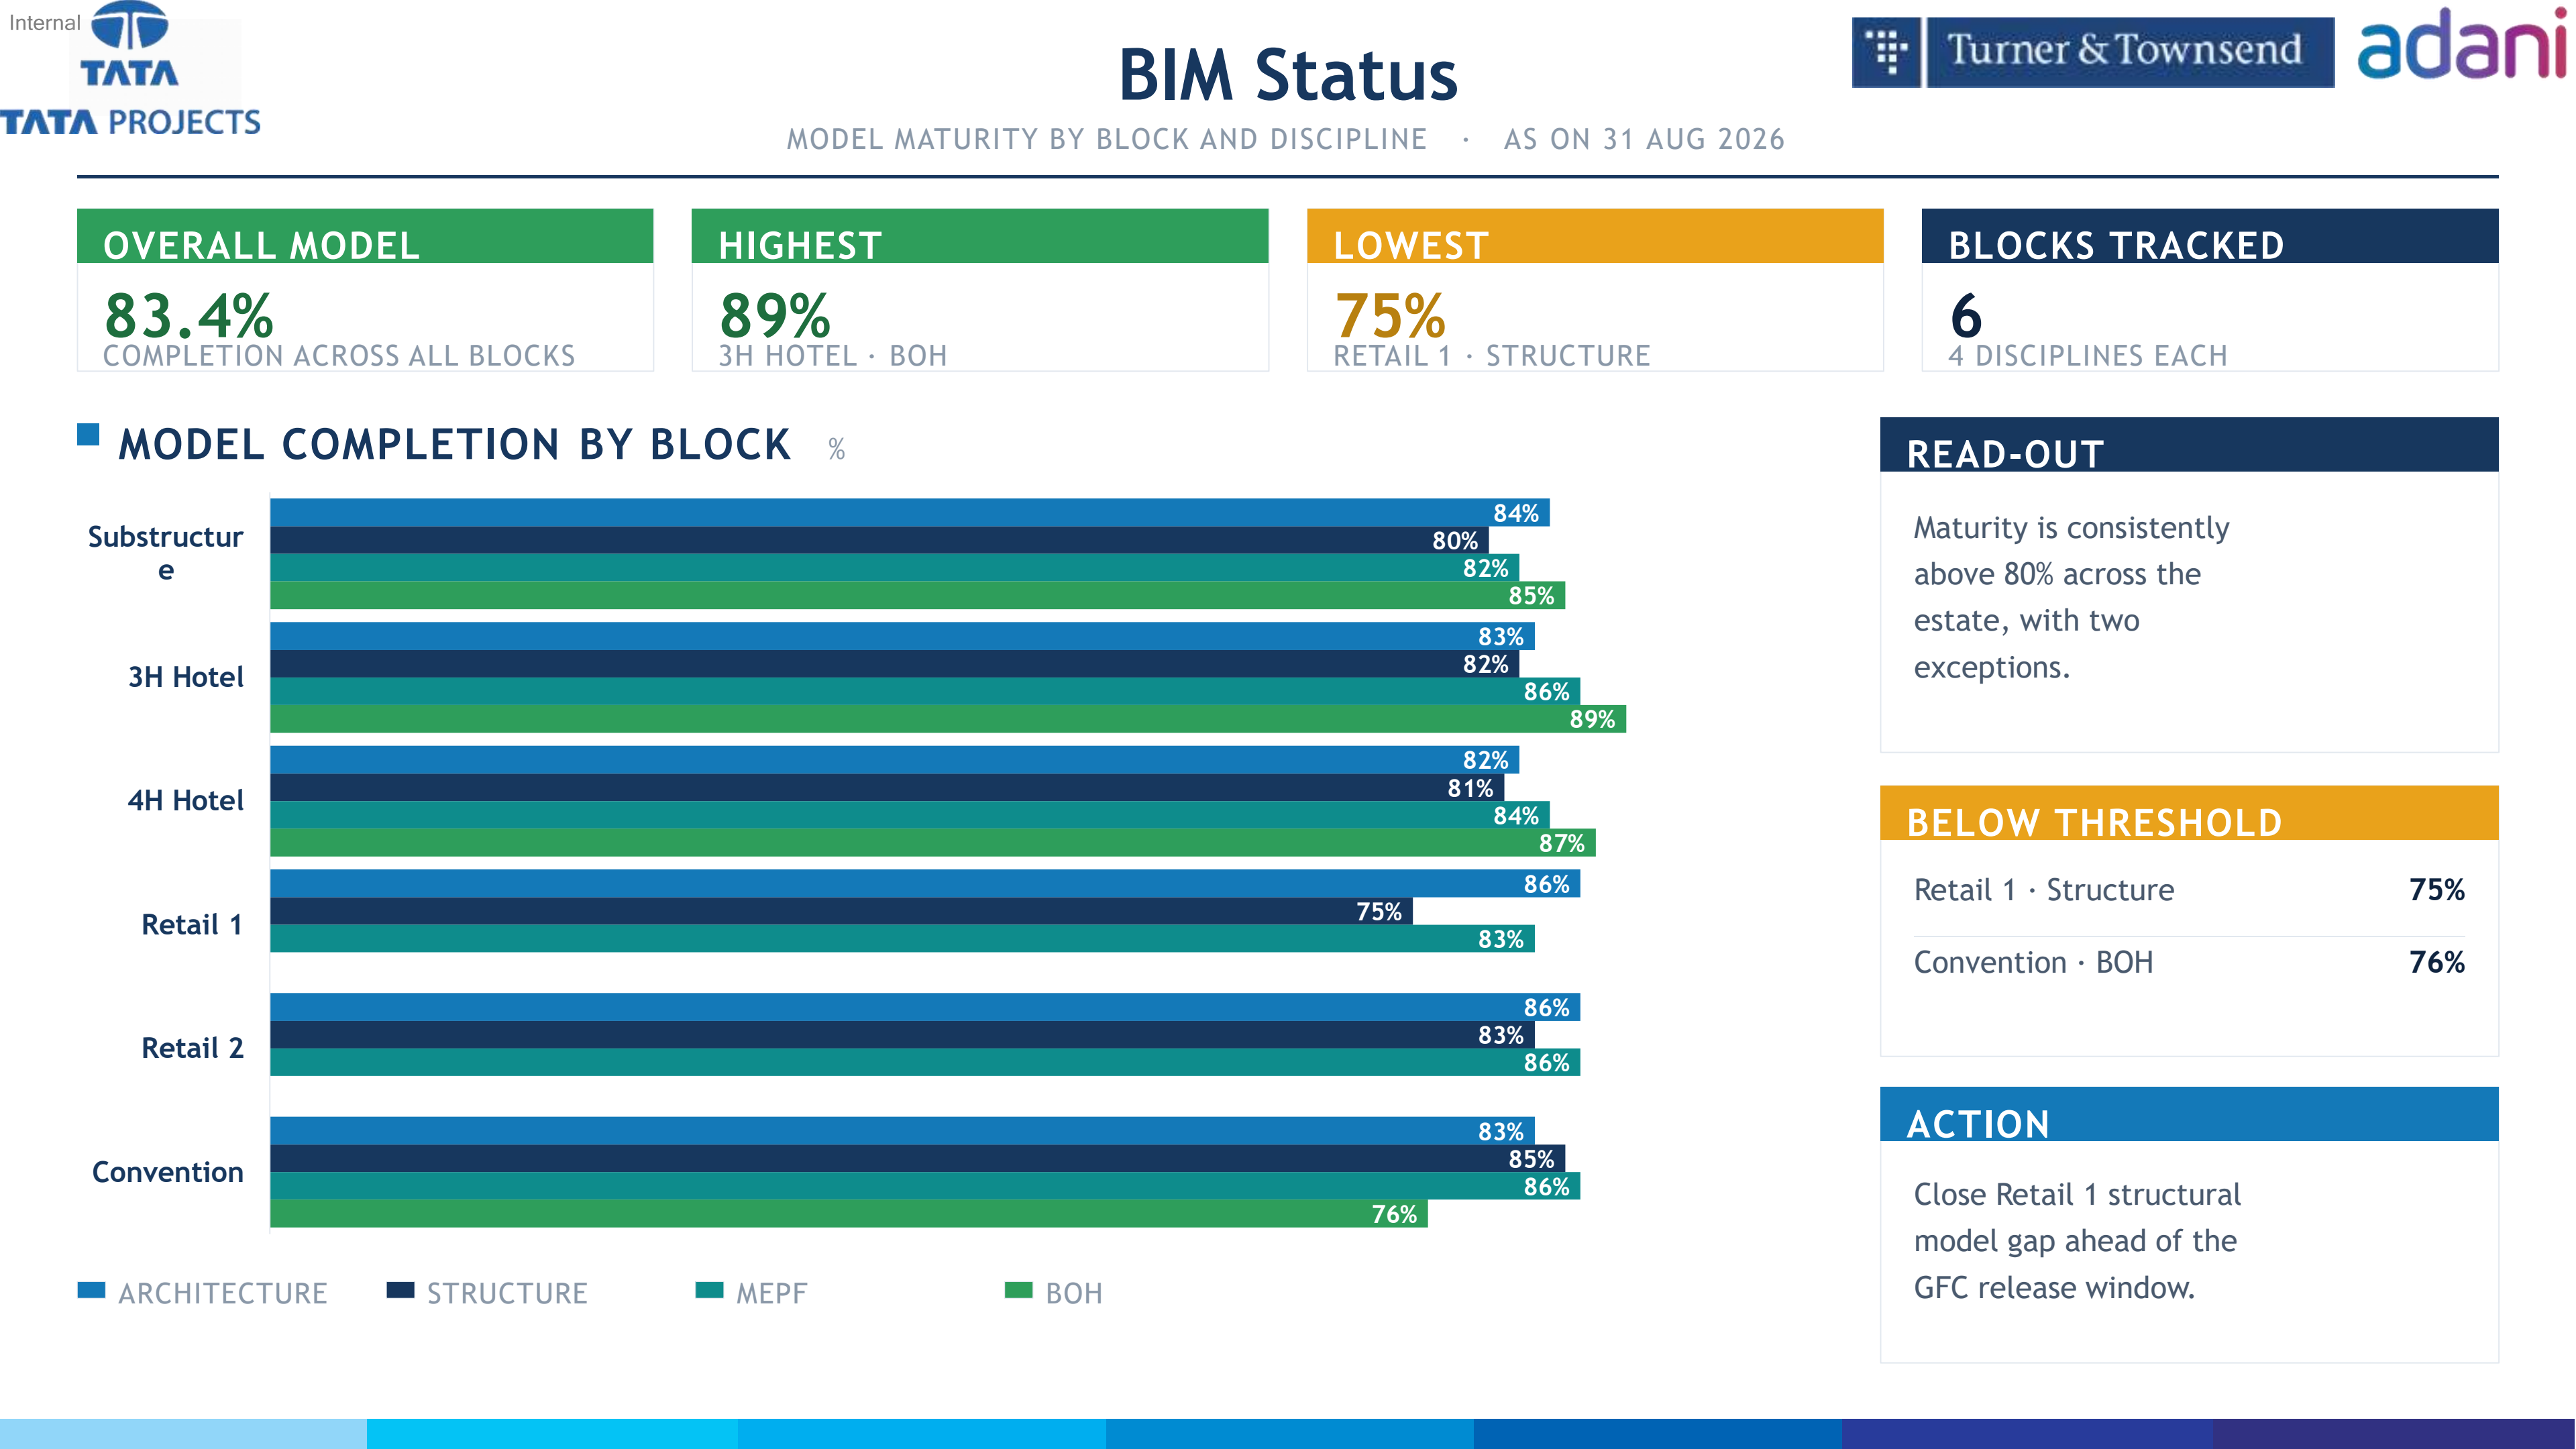

TOTAL PACKAGES

17

IN THE NSC SCOPE

INITIAL SUBMISSION

6

COMPLETED

DUE BY 15 SEP

5

IMMEDIATE WINDOW

FORWARD PIPELINE

6

20 SEP - 20 OCT

INITIAL SUBMISSIONS

Chillers & Pumps	07 Aug	DONE
Cooling Tower & Pumps	07 Aug	DONE
STP & ETP	28 Apr	DONE
DG Set	29 Jul	DONE
Transformer	14 Aug	DONE
Lifts & Escalators	25 Aug	DONE

IMMEDIATE DATES

PHE Complete	05 Sep	DUE
Fire Fighting	05 Sep	DUE
UPS	05 Sep	DUE
HT Panels	10 Sep	DUE
FAPA	15 Sep	DUE

FORWARD PIPELINE

HVAC Low Side	20 Sep
Electrical Low Side	20 Sep
HT & LT Cables	20 Sep
Bus Ducts	25 Sep
LT Panels	30 Sep
ELV Systems	20 Oct

NEXT DELIVERIES

Close PHE, Fire Fighting and UPS by 05 September 2026 to hold the September release window.

MONTH CONCRETE

3,025 m³

AGAINST 5,584 M³ PLAN

WORKMEN

1,032

AGAINST 1,000 PLAN

STAFF

142


DEPLOYED ON SITE

FOUNDATIONS

62 of 147

ACROSS THREE BLOCKS

■ AREA-WISE FOUNDATIONS

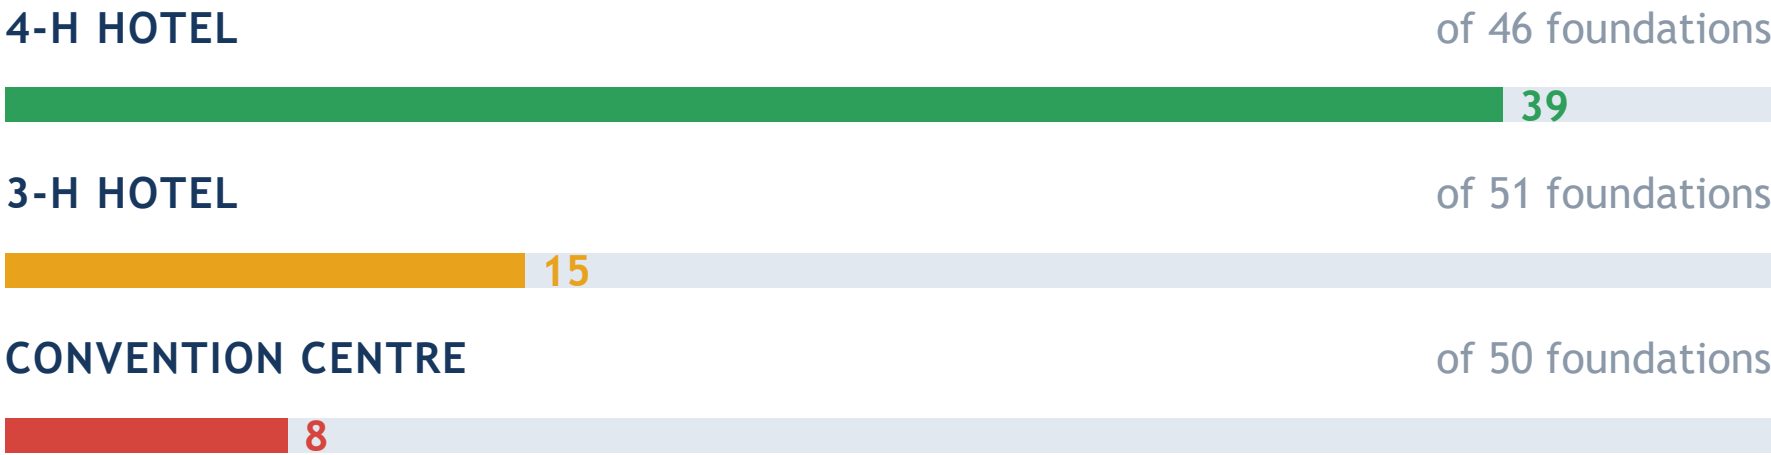

Retail 1 / 2 — awaiting handover

MILESTONES ACHIEVED

4-H: 24 of 77 columns cast

Convention Centre footing concreting commenced

Alternative RMC source approved

Reinforcement steel base rate approved 25 Aug 2026

■ CONSTRAINTS & RECOVERY

KEY CONSTRAINTS

Retail areas not released

Slow concrete supply and batching readiness

Monsoon disruption and delayed TMT rate approval

RECOVERY ACTIONS

Resequence around available handovers

Deploy alternate RMC source for mass concrete pours

Progress on available GFC and sustain manpower

Engineering: PT drawings availability

Construction: commence Retail blocks

SEPT MANPOWER PLAN

1,205

+173 NET AUGMENTATION

CURRENTLY AVAILABLE

1,032

WORKMEN ON SITE

TOWER CRANES

03 / 05

1 INSTALLED

WORKMEN SHEDS

5 × G+2

ALL ERECTED BY 31 OCT

WORKMEN CAMP DELIVERY

G+2 sheds

SHED PROGRAMME		
C1	22 Aug	OCCUPIED
B1	18 Sep	ERECTION
A1	04 Oct	PLINTH DONE
C2	06 Oct	PLINTH DONE
B2	31 Oct	WO ISSUED

MANPOWER



CAMP AMENITIES & SERVICES

DELIVERY STATUS		
Kitchen 1	—	COMPLETED
Cement Store	—	COMPLETED
Toilets (220)	—	20 DONE
Bath Sheds	13 Sep	SCHEDULED
Kitchen 2	10 Sep	SCHEDULED
Dining 2 / Store	15 Sep	SCHEDULED
Drain	26 Sep	SCHEDULED

PLANT & MACHINERY MOBILIZATION	
DG Sets	04 / 04
Trailer	02 / 02
Vibro Roller	01 / 01

Internal



TATA

TATA PROJECTS

Update on Last MOM

MINUTES OF MEETING · ACTION TRACKER · PAGE 1 OF 3

Turner & Townsend



SR.	POINT DISCUSSED	DISCUSSION / OBSERVATION	ACTION BY	TARGET DATE	TPL UPDATE
1	Design Coordination – PT Slab & MEP Cutouts	PT slab design delayed by unresolved MEP sleeves, cutouts and openings. These must be coordinated before design completion; all consultants to sign off on drawings before proceeding.	TPL – Rakesh Kumar Garg	For action	All MEP cut-outs and sleeves incorporated in the B2 PT layout and approved by all consultants. B2 PT details issued to J+W on 10 Aug; comments received 13 and 21 Aug. GA layout resubmitted 25 Aug; PT tendon layout per peer-review comments submitted 31 Aug.
	Vendor & Consultant Coordination	Performance shortfall from EcoFirst and Edifice; coordination issues persist despite multiple workshops and escalations. A rigorous workshop approach with direct TPL involvement was agreed.	TPL – Rakesh Kumar Garg	For action	TPL MEP team stationed at the EcoFirst office from 10 to 21 Aug to coordinate all B3 and B2 services and finalise the MEP input for the PT design.
	Workshop Planning & Action Items	Focused discussions to be held twice weekly from the following week to identify grievances, shortfalls and support required, with EcoFirst and all consultants at the table.	TPL – G V Radha Krishna	From 10 Aug 26	Workshop held every Tuesday; additional sessions arranged as required.
	BIM versus 2D Design Methodology	BIM is used across all areas except Basements 1 and 2 of the 4-Star Hotel, where 2D drawings are an interim measure to expedite progress; those areas will be brought into BIM compliance later. Full multidisciplinary coordination is required before design sign-off.	TPL – Rakesh Kumar Garg	For action	Agreed.

Internal

TATA

TATA PROJECTS

Update on Last MOM

MINUTES OF MEETING · ACTION TRACKER · PAGE 2 OF 3

Turner & Townsend

adani

SR.	POINT DISCUSSED	DISCUSSION / OBSERVATION	ACTION BY	TARGET DATE	TPL UPDATE
2	Detailed Design Closure	Detailed Design is not closed – coordinated layouts and MEP-to-structural coordination remain outstanding.	TPL – Rakesh Kumar Garg	For action	Close coordination in progress. FAPA and Fire Fighting closed 26 Aug 26; Plumbing closed 27 Aug 26; Electrical and HVAC to close by 11 Sep 26.
	B3 Ceiling Layout	Complete and finalise the Basement 3 ceiling coordinated layout by 15 August 2026.	TPL – Rakesh Kumar Garg	15-08-26	B3 ceiling coordinated with all consultants and submitted on 02 Sep 26.
	Design Input Tracker	Prepare and present a tracker for all design inputs and clarifications to streamline communication across consultants.	TPL – Sudhanshu Shukla	13-08-26	Tracker is being maintained.
	VE Façade Intent	All clarifications on the updated VE façade intent agreed by stakeholders; the BIM model to be reshared with Edifice, with further coordination by TPL.	ALACL / TPL	07-08-26	BIM model accepted by the Edifice team for further working.
	Meeting Agenda	EcoFirst and Edifice meeting agenda points to be shared by TPL prior to the meeting.	TPL – Rakesh Kumar Garg	For action	Noted.
	Landscape & External Development	Design cell to update the status of landscape and external development, coordinated with MEP works and completed.	TPL – Sudhanshu Shukla	For action	Landscape presentation held 27 Aug; Adani comments received the same day and are being coordinated.
	Utility Rooms	Utility-room coordinated drawings to be completed within the same workshop.	TPL – Sudhanshu Shukla	For action	Agreed.
	Leak-Proof Cut-Out	TPL to share a typical detail of the leak-proof cut-out.	TPL – Sudhanshu Shukla	21-08-26	Typical detail of the leak-proof cut-out submitted on 27 Aug 26.

Internal

TATA

TATA PROJECTS

Update on Last MOM

MINUTES OF MEETING · ACTION TRACKER · PAGE 3 OF 3

Turner & Townsend

adani

SR.	POINT DISCUSSED	DISCUSSION / OBSERVATION	ACTION BY	TARGET DATE	TPL UPDATE
3	Vendor List Submission & Approval	Official vendor lists for all packages to be submitted by Monday without further discussion; critical packages must be awarded in the current quarter.	TPL – G V Radha Krishna	For action	Submission made.
	Tendering & Technical Evaluation Workflow	Workflow reviewed – design review, BOQ preparation, technical and commercial evaluation and work-order issue – with roles assigned to the cost consultant, PMC, D&B partner and other stakeholders.	TPL – Vivek Srivastava	15-08-26	Noted; detailed information flow submitted.
	Package Strategy & Single Contractor	Single-contractor approach considered for certain MEP high-side and low-side works to streamline execution and reduce the risk of delay from contractor failure.	TPL – Vivek Srivastava	13-08-26	Noted; the strategy as advised is being followed.
	RFP Finalisation	STP, MEPF and Façade RFP documents to be finalised and vendors onboarded within this financial year, forming part of the FY cashflow.	TPL / T&T / Adani	07-08-26	RFPs for the various MEPF packages including STP submitted. Status tracker updated.
	NSC Vendor Onboarding	TPL to submit independently its proposal for onboarding NSC vendors; all NSC package vendor lists were due on 10 Aug.	TPL – Vivek Srivastava	For action	Submission made on 24 Aug 26.
4	Physical & Financial Progress Review	Cumulative work done, budgeted cost and progress S-curves reviewed. Discrepancies between planned and actual progress noted, particularly in concrete and steel quantities, with acceleration strategies discussed.	TPL – Vivek Srivastava	10-08-26	Submitted through the Revamp Plan – mailed 04 Aug, discussed in detail 08 Aug and signed submission made 29 Aug 26.
	Resource & Quantity Breakdown	Detailed breakdowns of reinforcement steel, concrete and other resources presented. Adani advised further analysis of monthly targets against actual achievement to ensure alignment with the schedule.	TPL – Vivek Srivastava	For action	Noted.

Internal

TATA

TATA PROJECTS

September 2026 Plan

PLANNED VALUE, QUANTITIES AND WEEKLY DISTRIBUTION

Turner & Townsend

adani

TOTAL PLANNED VALUE

₹37.5 Cr

SEPTEMBER 2026

SUPPLY

₹24.0 Cr

64% OF PLAN

SERVICE

₹12.5 Cr

33% OF PLAN

DESIGN

₹1.0 Cr

3% OF PLAN

MAJOR ITEMS

₹ Cr

VALUE BREAKDOWN

Reinforcement Supply

₹17.2 Cr

Reinforcement Service

₹8.0 Cr

M40 Supply

₹6.2 Cr

M40 Service

₹3.8 Cr

Design Review

₹1.0 Cr

Other Activities

₹1.3 Cr

WEEKLY DISTRIBUTION

M40 CONCRETE AND REINFORCEMENT

WEEK

M40 (M³)

REBAR (MT)

W1

1,943

750

W2

2,553

750

W3

1,946

500

W4

3,584

1,000

VALUE MIX

Supply

24.0

Service

12.5

Design

1.0

CRITICAL QUANTITIES

M40 Supply

10,344 m³

M40 Service

10,344 m³

Reinforcement

3,000 MT

M10 Supply + Service

405 m³

September 2026 Pour Plan

BLOCK-WISE POUR PLAN AND RCC QUANTITIES · SEPTEMBER 2026



Building	Footing Nos	RCC Qty.
3H	CF25	133
3H	CF31	959
3H	CF25A	105
3H	CF25B	108
3H	CF26A	1138
3H	CF31A	959
3H	CF21	982
3H	CF23A	223
CC	CF13A	393
CC	CF34	113
CC	F8-4nos	110
CC	F12-3nos	187.5
CC	F13	67.6
CC	F1	12.5
CC	CF19	1594
	Couulum/Shear Wall	100
	Total-	10379.5

Building	Footing Nos	RCC Qty.
4H	CF14A	140
4H	CF1K	90
4H	CF32A	61
4H	F6	22
4H	CF1D	126
4H	CF32	1305
4H	CF26B	1223
4H	F5-2nos	36.4
4H	F8-2nos	55
4H	F10-3nos	136.5

Internal  TATA PROJECTS	Statutory Compliance CLOSURE PATH AND OPEN POSITIONS · AUGUST 2026		
OPEN POSITIONS 3 OF 4 TRACKED ITEMS	CLOSED 1 POLICY AMENDMENT	CLIENT INPUT PENDING PENDING BG AMENDMENT · 21 AUG 2026	NEXT MILESTONE 05 SEP BOCW RECEIPT EXPECTED
COMPLIANCE CLOSURE PATH			
ITEM 01 BG Amendment ALACL INPUT PENDING Details requested from client on 21 Aug 2026. Follow up for ROC, NCLT, MCA, board resolution and supporting novation documents.	ITEM 02 Policy Amendment UPDATED CAR and Marine policies amended following novation. No further action required.	ITEM 03 Labour Licence CLOSURE REQUIRED Compliance closure up to July 2026 pending. Complete formalities and record statutory acknowledgement.	ITEM 04 BOCW EXPECTED 05 SEP Receipt awaited. Track receipt and close supporting documentation immediately.

Good Practices

ENVIRONMENT, HEALTH AND SAFETY · AUGUST 2026



Turner & Townsend

adani



Illumination inspection at the work front



Noise level monitoring – 54.5 dB



Noise level monitoring – 54.0 dB



Pedestrian access board displayed near Gate No. 02



Illumination inspection – night shift

HSE Good Practices

VEHICLE SAFETY AND RECOGNITION · AUGUST 2026



Seven Mirror Concept implemented on all heavy vehicles



Safety Conscious Person of the Month displayed

Environmental Initiative

SIGNAGES PRODUCED FROM SCRAP PLYWOOD · AUGUST 2026



Deep excavation caution board




Deep excavation caution board – work front



Speed limit and PPE zone signage



Site safety notice board

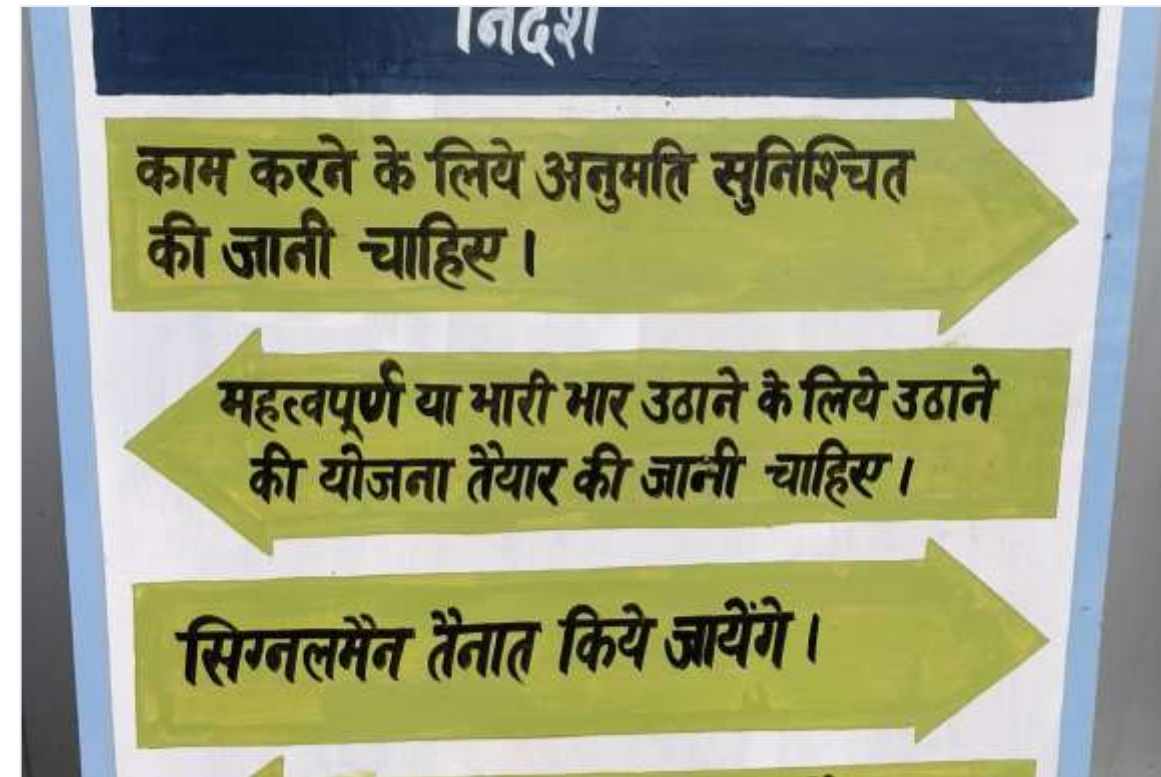

Lifting safety instruction board



Safety and welfare signage board

Tool Box Talks

DAILY BRIEFINGS DELIVERED ON SITE • AUGUST 2026



Emergency preparedness and response — 21 Aug 26



Right way of using a full body harness — 11 Jul 26



Hazards in bar bending and cutting activity — 07 Aug 26



Tool box talk at the work front — 11 Aug 26



Site safety rules — 27 Aug 26



Full workforce briefing before shift start

Safety Posters and Signages

SITE COMMUNICATION • AUGUST 2026



Safety briefings across the workforce



Child labour prohibited — statutory notice



Workmen accommodation guidelines board



Behavioural safety mural at the accommodation block



Speed limit and work-in-progress signage with blinking lights near the concrete plant

Mock Drill

WORKER HIT BY A MOVING VEHICLE • EMERGENCY RESPONSE REHEARSAL



Emergency response, casualty handling and evacuation sequence rehearsed on site

Quality Indicators

LEADING AND LAGGING QUALITY PERFORMANCE · AUGUST 2026

FIRST TIME RIGHT INDEX

88%

PROJECT OUTCOME

TRAINING IMPARTED

74

EFFORT HOURS

GOOD / BEST PRACTICES

16

RECORDED THIS MONTH


DEVIATION CLOSURE TAT

19.9

DAYS AVERAGE


LEADING INDICATORS

proactive quality inputs

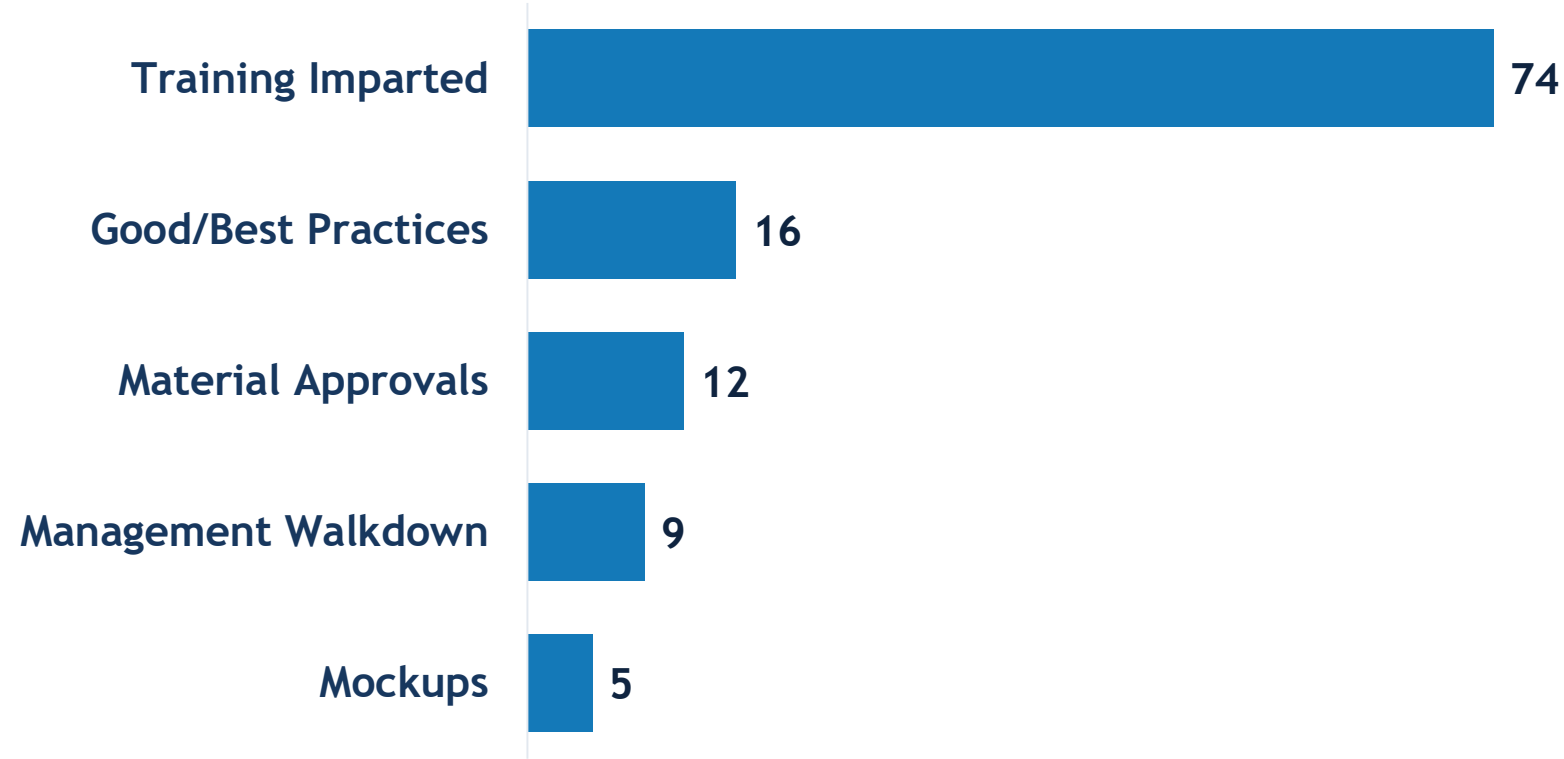


LAGGING INDICATORS

actual project outcomes

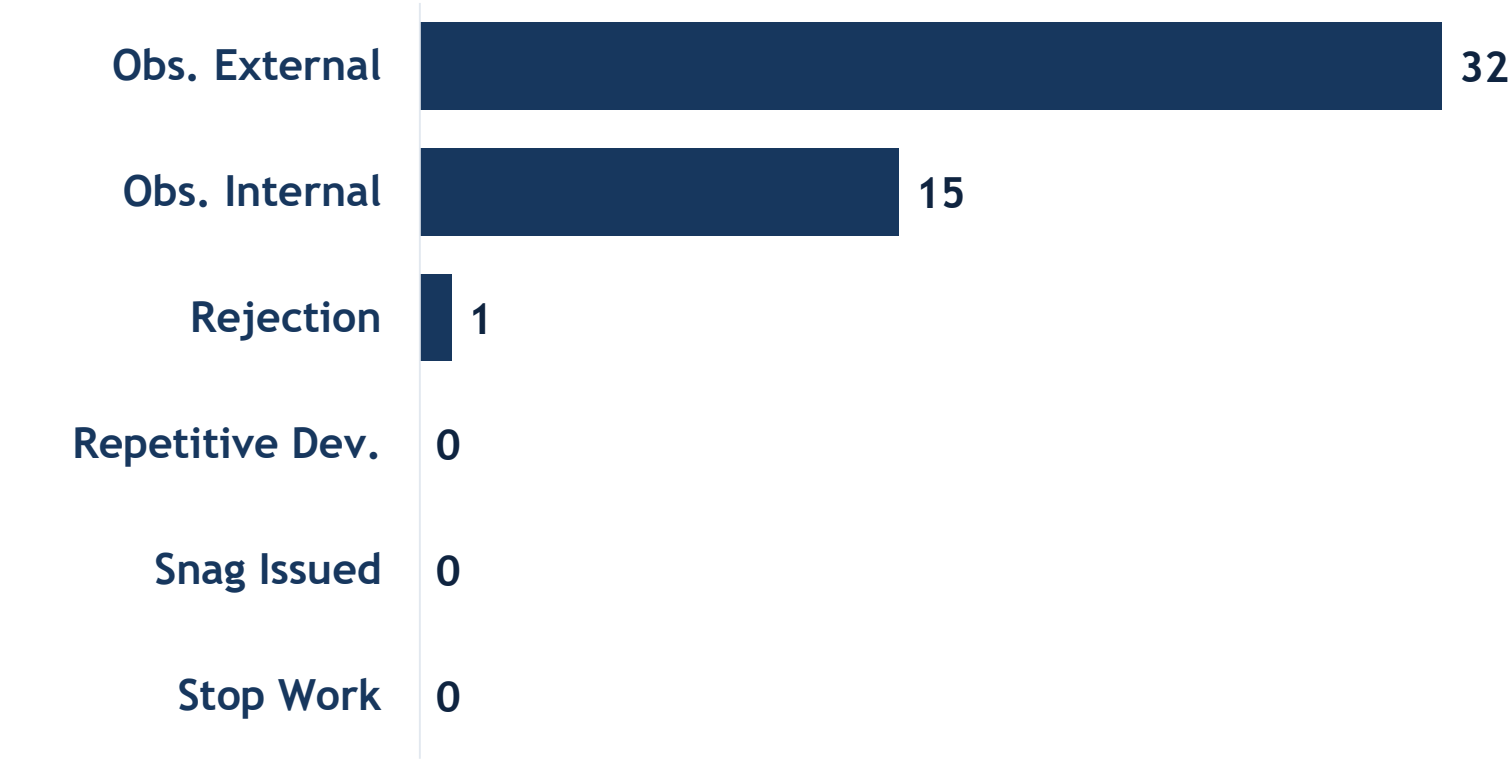

READ-OUT

Proactive quality investment translates directly into near-perfect execution and zero-defect outcomes.

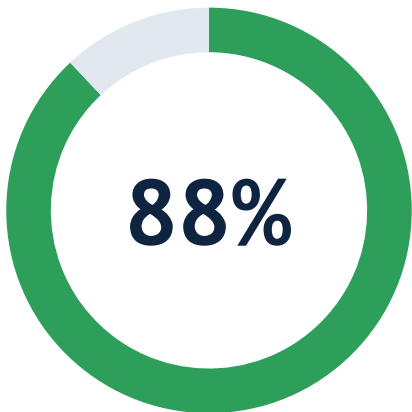

88%

FIRST TIME RIGHT

Skill Ratio	0.60
Flash Report	0
Deviation Closure in TAT	19.9 days

OBSERVATIONS CLOSED	OPEN OBSERVATIONS	NCR CLOSED	TRAININGS
24 OF 32 RAISED	8 UNDER ACTION	103 OF 123 RAISED	44 450 MAN-HOURS

OBSERVATION CLOSURE



NCR CLOSURE



TRAINING DELIVERED

CUMULATIVE	
Cumulative trainings	44
Cumulative man-hours	450.02

NOTE

Source charts on this slide previously linked to an external SharePoint workbook and would not refresh outside the TPL tenant. They are now embedded and travel with the deck.



Steel coupler threading in progress



Go / No-Go gauge test after coupler threading



Curing compound applied uniformly after pouring



Curing compound coverage across the pour area



Sample installation of Formstop to avoid column starters



Formstop fixing at the column starter location



Steel cutting and bending training



Steel cutting and bending training



Steel threading training



Threading machine demonstration



Coupler threading quality check



Concrete pouring and finishing training



Site quality induction



Site quality induction – classroom session



Tool box training at the work front



Workmen briefing at the work front

4 Star Hotel Progress

JULY 2026 VERSUS AUGUST 2026




July 2026



August 2026

3 Star Hotel Progress

JULY 2026 VERSUS AUGUST 2026

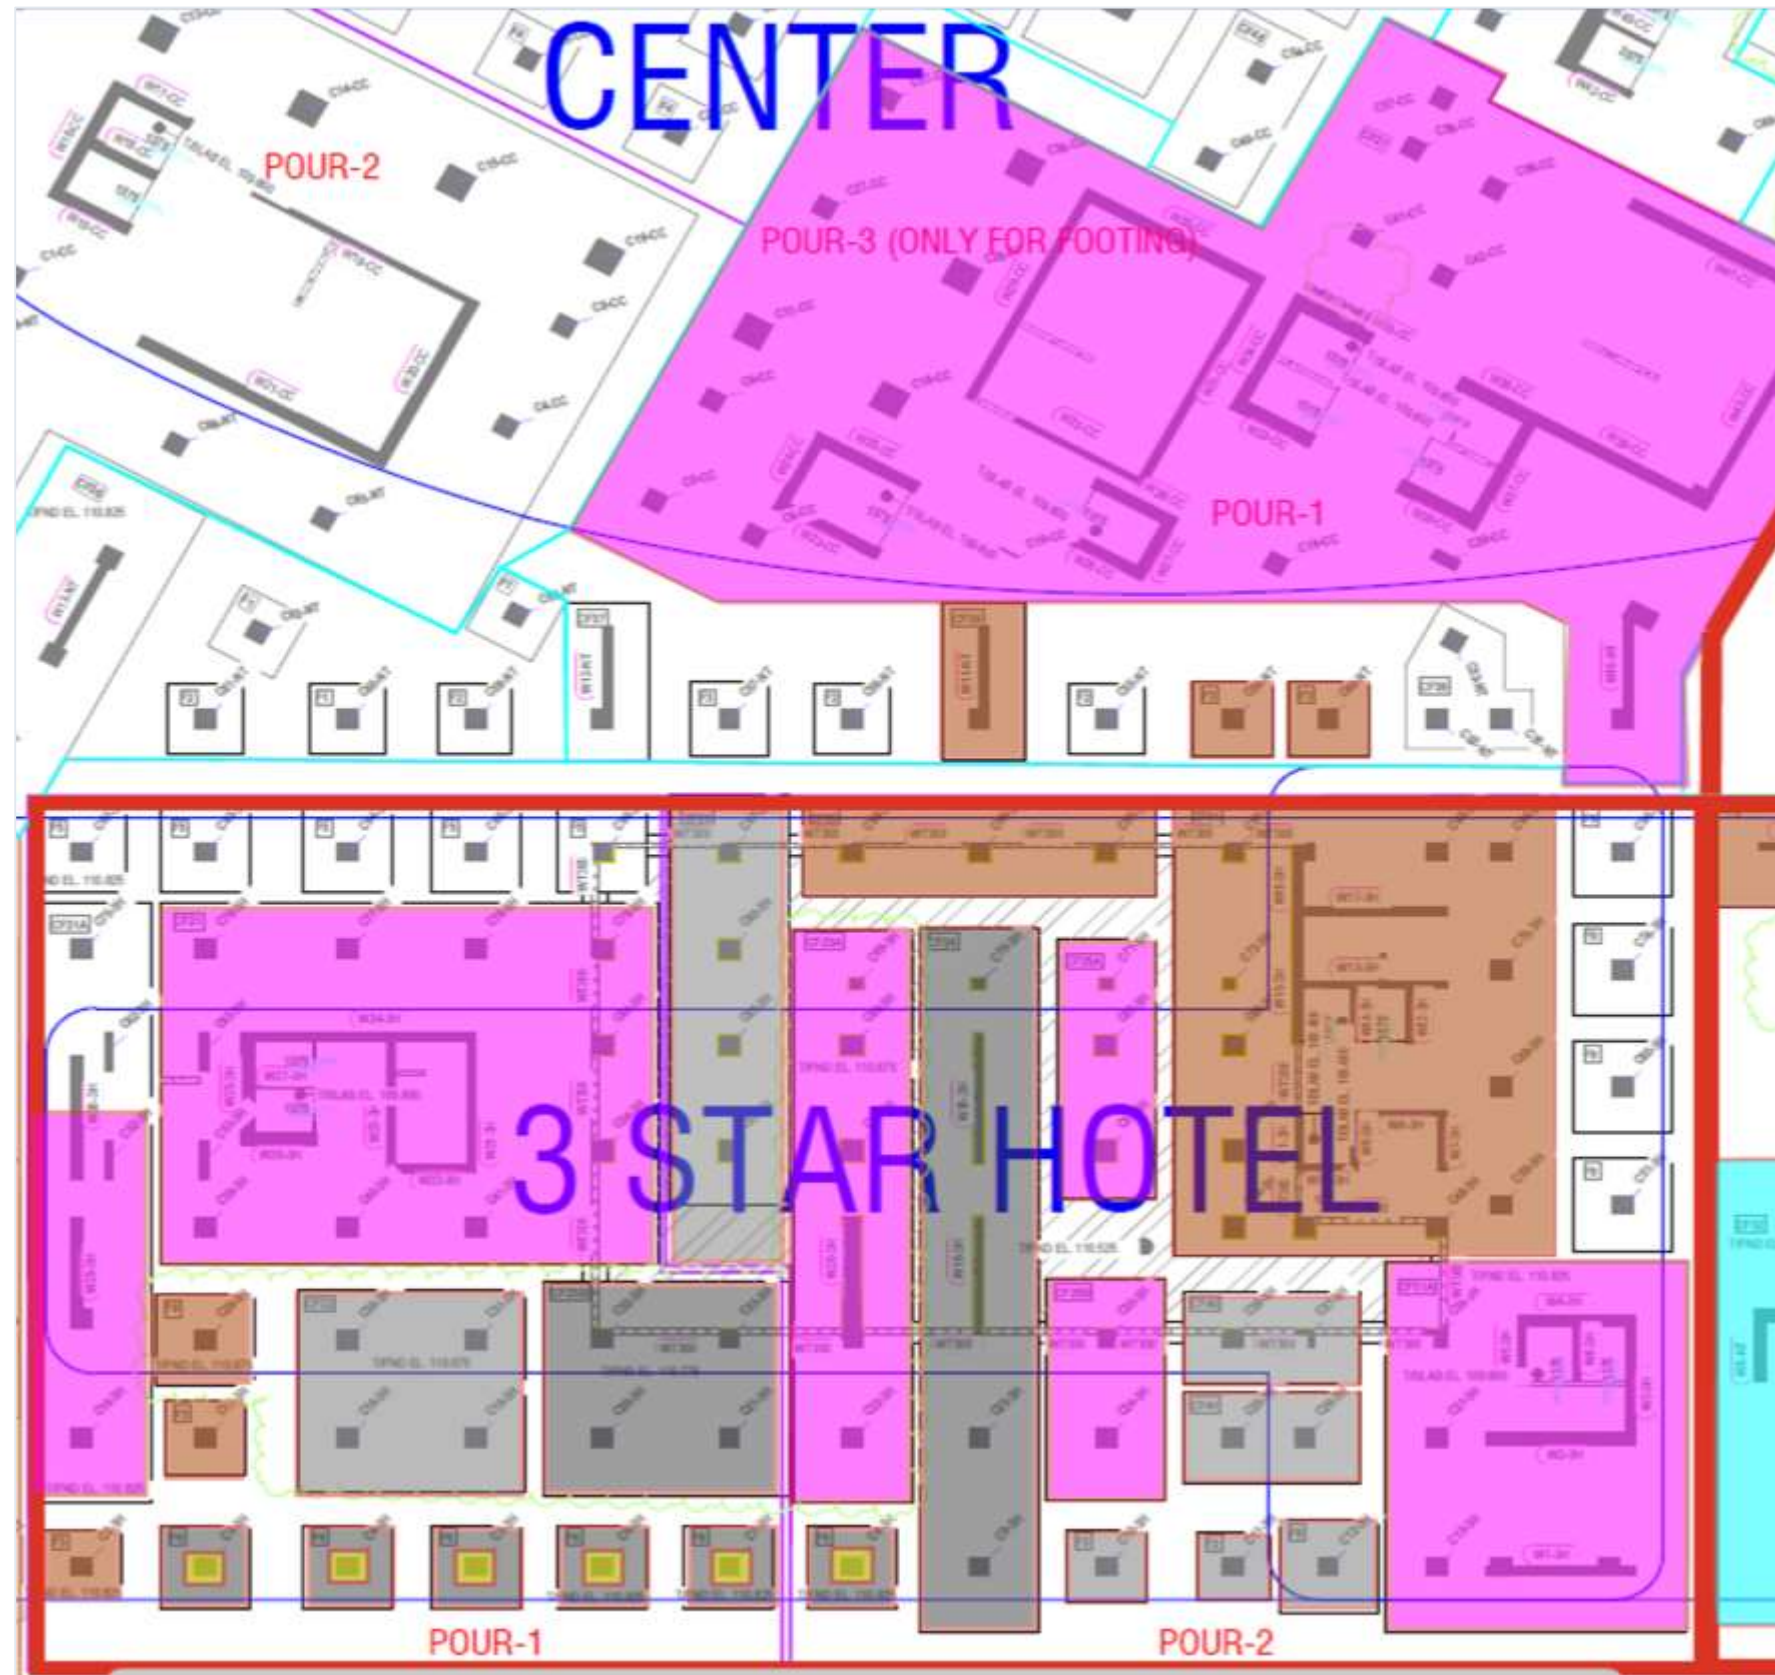

July 2026



August 2026

Convention Centre Progress

JULY 2026 VERSUS AUGUST 2026



July 2026



August 2026

Updates

PROGRESS · QUALITY · PHOTOGRAPHS

Progress Photos

FOUNDATION COMPLETION BY AREA · AUGUST 2026



4 Star area — 39 of 46 footings completed



4 Star area — column and pedestal casting



3 Star area — 15 of 51 footings completed



3 Star area — raft and column reinforcement



Convention Centre — 08 of 50 footings completed

Site Infrastructure

ENABLING WORKS AND WELFARE • AUGUST 2026



Safety park and information kiosk



Workmen rest area and pedestrian walkway



Tower crane — operational



Site toilet facility for workmen

Workmen Camp & Steel Yard

CAMP DELIVERY AND MATERIAL HANDLING · AUGUST 2026



Camp development and toilet shed



Workmen shed C1 — G+2



Medical and EHS room



Steel yard

Thank You

ADANI LUCKNOW AIRPORT CITY · MONTHLY REVIEW · AUGUST 2026
